

PERCY TREYVAUD MEMORIAL PARK SPORT FACILITIES CONSTRUCTION

CONSTRUCTION UPDATE 14

September 2023

Recap on works to date

Excitement is building (literally) as we head down the home stretch of construction at the Percy Treyvaud Memorial Park multipurpose sport and recreation facility. The Rob Roy Road footpath has reopened after we completed the landscaping and lighting works. Thank you for your patience. Indoors, we've installed new basketball rings, put down court markings, and sealed it all with a final floor coating. Around the courts is tiered seating ready for the first supporters. In the pavilion, we've installed all the doors, finished the bathrooms, wired in the lighting, and laid the carpet tiles. In August, we completed 11,740 hours. That brings our total hours worked since January 2022 to 160,340.

What to expect in the month ahead

External carpark closure


The external carpark will be closed to make way for the new carpark. We expect the work to take five weeks, when we'll be almost at the project finishing line.

Sports courts

We'll add four scoreboards for the indoor courts. And we'll finish off the tennis courts and bowling green, ahead of painting and carpeting.

Pavilion

As the internal scaffolding comes down, we'll finish plastering and painting the walls. Work on the upper floor socialising areas will continue. We'll install and lay outdoor pavers, creating a communal space.

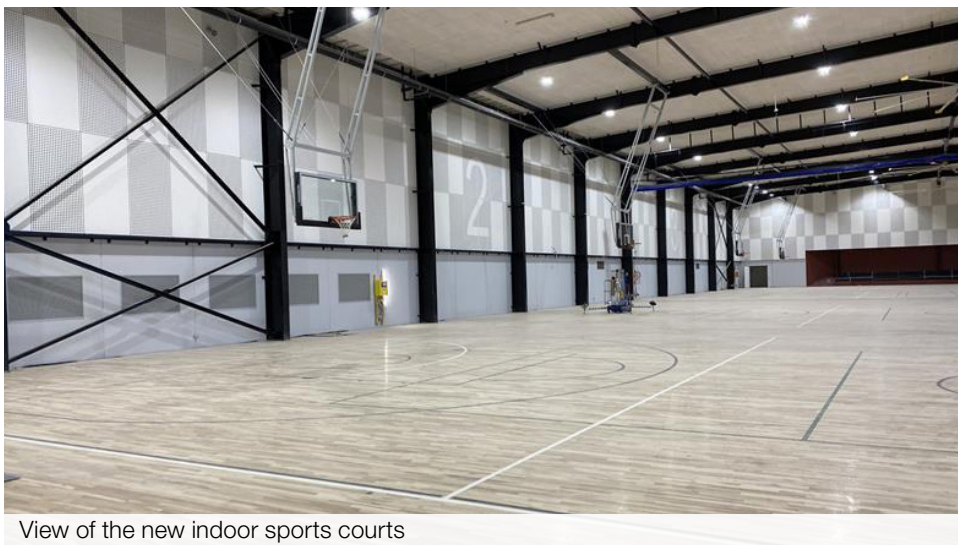

WORK SITE

Pedestrian access within the worksite is restricted during the project, in accordance with WorkSafe and OH&S practices.

COVID-19

We are working in accordance with Victorian Government COVID-19 guidelines, and within strict health and safety protocols.

stonnington.vic.gov.au/ptmp

We recognise works of this nature may cause some inconvenience and we thank you for your patience and understanding as we deliver this important community sports facility.



City of
STONNINGTON

Park and facility access

- » The oval and playground areas remain open
- » Playground access will remain throughout construction, via the Rob Roy Road footpath
- » For everyone's safety, we have fenced the construction area, and restricted access.

Chart our progress

To see how works are progressing, view the site photo gallery at stonnington.vic.gov.au/ptmp

Working with you

ADCO is committed to minimising the impacts of our construction works on local residents and the environment. We'll continue to keep you updated as construction progresses.

If you have any questions or concerns about construction, please contact ADCO Construction:

e: ptmp@stonnington.vic.gov.au

p: 0428 802 501

Sign up for digital project updates

If you would prefer updates about the project via email, please visit stonnington.vic.gov.au/ptmp where you can sign up to the PTMP Project eNewsletter and have your postal address removed from the mailing list.

Location

Percy Treyvaud Memorial Park, Chadstone Road, Malvern East.

Construction timeline

February 2022 to end-2023

(estimated two-year build).

Follow the art trail

Walk along the north side of the construction site, between Chadstone and Quentin roads, to view a gallery of artworks from Malvern Valley Primary School students. The young artists have created 240 self-portraits depicting themselves enjoying their favourite sport.

Then and now: our progress over the last year



Then: preparing the site in July 2022



Now: overlooking the new canopied bowling green
